

US-176 Widening Phase 1 One Cent Sales Tax Program

August 2025

Project Information

The US-176 Widening Phase 1 Project is a bid-build project that includes widening a total of 4.7 miles of US-176 between Sheep Island Rd. & US-17A from 2 to 4 lanes. It includes turn lanes, raised concrete medians, signal & intersection improvements, as well as extensive water & sewer relocations.

Awarded To: L. Dean Weaver Company

Original Contract Amount: \$52,891,045.94


Current Contract Amount: \$51,453,259.20

Scheduled Completion Date: November 14, 2025


PROJECT STATUS



TIME

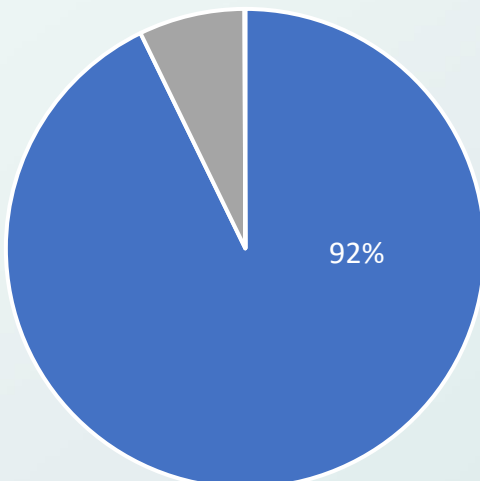

WORK TO DATE:
\$34,918,429.20

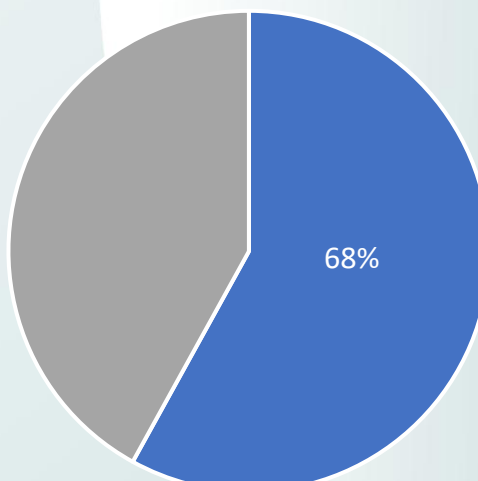

PROJECT ACTIVITIES

In-Contract Utility Relocation

- ❖ In-contract BCWS water installation has been substantially completed. Final walk-through will be scheduled for September 2025.

Construction Activities

- ❖ Storm installation has been completed on St. James Ave. and is almost complete on US 17A.
- ❖ L. Dean Weaver Co. is working to tie in all concrete sections and pave all asphalt base between Cane Bay / North Creek Drive intersection and Domingo Drive to allow Sanders to continue with intermediate course paving.
- ❖ Signal work at Nexton Pkwy and Cane Bay Blvd intersections has been completed (signal adjustments to be made once traffic is in final configuration).
- ❖ Change Order 09 (Marshall Acres Drive Turn Lane) was executed to add \$114,566.96 and 24 days to the Contract.

Progress meetings occur every other Thursday at 10am at the Berkeley County Engineering/Admin Building

Project Office

*4016 Salt Pointe Parkway
North Charleston, SC 29405*

For project related inquiries, contact:

Michael Weekley

Michael.Weekley@ice-eng.com

843-238-5441

*This report was prepared by
Infrastructure Consulting and Engineering*
